

TITLE:

AVAILABLE LANGUAGE: IT

# COSTRUZIONE DELL'IMPIANTO EOLICO DI "TRAPANI 3"

## PROGETTO DEFINITIVO

### Cronoprogramma



File: GRE.EEC.R.73.IT.W.14703.00.033.00 - Cronoprogramma.pdf

REV.	DATE	DESCRIPTION	PREPARED	VERIFIED	APPROVED
00	18/12/2020	Prima emissione	D. Gradogna	E. Castiello	L. Lavazza


#### GRE VALIDATION

	Support Team (GRE)	A. Puosi (GRE)
COLLABORATORS	VERIFIED BY	VALIDATED BY

PROJECT / PLANT <b>Trapani 3</b>	GRE CODE																			
	GROUP	FUNCTION	TYPE	ISSUER	COUNTRY	TEC	PLANT				SYSTEM	PROGRESSIVE	REVISION							
	<b>GRE</b>	<b>EEC</b>	<b>R</b>	<b>7</b>	<b>3</b>	<b>I</b>	<b>T</b>	<b>W</b>	<b>1</b>	<b>4</b>	<b>7</b>	<b>0</b>	<b>3</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>3</b>	<b>3</b>	<b>0</b>	<b>0</b>
CLASSIFICATION	<b>PUBLIC</b>					UTILIZATION SCOPE	<b>BASIC DESIGN</b>													


ID	Task Name	Duration	Predecessors	Start	2022				2023					
					January	April	July	October	January	April	July	October	January	April
1	<b>IMPIANTO EOLICO TRAPANI 2</b>	<b>559 days</b>		Tue 01/03/22	[Timeline bar from Jan 2022 to Apr 2023]									
2	Allestimento cantiere	5 days		Tue 01/03/22	[Timeline bar from Jan 2022 to Jan 2022]									
3	<b>REALIZZAZIONE NUOVO IMPIANTO</b>	<b>528 days</b>		Tue 08/03/22	[Timeline bar from Jan 2022 to Apr 2023]									
4	Adeguamenti viabilità esistente	30 days	2	Tue 08/03/22	[Timeline bar from Jan 2022 to Feb 2022]									
5	<b>Realizzazione strade e piazzole</b>	<b>200 days</b>		Tue 05/04/22	[Timeline bar from Jan 2022 to Oct 2022]									
6	Strada T3_01	10 days	4FS-10 days	Tue 05/04/22	[Timeline bar from Jan 2022 to Jan 2022]									
7	Piazzola T3_01	10 days	6	Tue 19/04/22	[Timeline bar from Jan 2022 to Jan 2022]									
8	Strada T3_02	10 days	7	Tue 03/05/22	[Timeline bar from Jan 2022 to Jan 2022]									
9	Piazzola T3_02	10 days	8	Tue 17/05/22	[Timeline bar from Jan 2022 to Jan 2022]									
10	Strada T3_03	10 days	9	Tue 31/05/22	[Timeline bar from Jan 2022 to Jan 2022]									
11	Piazzola T3_03	10 days	10	Tue 14/06/22	[Timeline bar from Jan 2022 to Jan 2022]									
12	Strada T3_04	10 days	11	Tue 28/06/22	[Timeline bar from Jan 2022 to Jan 2022]									
13	Piazzola T3_04	10 days	12	Tue 12/07/22	[Timeline bar from Jan 2022 to Jan 2022]									
14	Strada T3_05	10 days	13	Tue 26/07/22	[Timeline bar from Jan 2022 to Jan 2022]									
15	Piazzola T3_05	10 days	14	Tue 09/08/22	[Timeline bar from Jan 2022 to Jan 2022]									
16	Strada T3_06	10 days	15	Tue 23/08/22	[Timeline bar from Jan 2022 to Jan 2022]									
17	Piazzola T3_06	10 days	16	Tue 06/09/22	[Timeline bar from Jan 2022 to Jan 2022]									
18	Strada T3_07	10 days	17	Tue 20/09/22	[Timeline bar from Jan 2022 to Jan 2022]									
19	Piazzola T3_07	10 days	18	Tue 04/10/22	[Timeline bar from Jan 2022 to Jan 2022]									
20	Strada T3_08	10 days	19	Tue 18/10/22	[Timeline bar from Jan 2022 to Jan 2022]									
21	Piazzola T3_08	10 days	20	Tue 01/11/22	[Timeline bar from Jan 2022 to Jan 2022]									
22	Strada T3_09	10 days	21	Tue 15/11/22	[Timeline bar from Jan 2022 to Jan 2022]									
23	Piazzola T3_09	10 days	22	Tue 29/11/22	[Timeline bar from Jan 2022 to Jan 2022]									
24	Strada T3_10	10 days	23	Tue 13/12/22	[Timeline bar from Jan 2022 to Jan 2022]									
25	Piazzola T3_10	10 days	24	Tue 27/12/22	[Timeline bar from Jan 2022 to Jan 2022]									
26	Strada T3_11	10 days	4FS-10 days	Tue 05/04/22	[Timeline bar from Jan 2022 to Jan 2022]									
27	Piazzola T3_11	10 days	26	Tue 19/04/22	[Timeline bar from Jan 2022 to Jan 2022]									
28	Strada T3_12	10 days	27	Tue 03/05/22	[Timeline bar from Jan 2022 to Jan 2022]									
29	Piazzola T3_12	10 days	28	Tue 17/05/22	[Timeline bar from Jan 2022 to Jan 2022]									
30	Strada T3_13	10 days	29	Tue 31/05/22	[Timeline bar from Jan 2022 to Jan 2022]									
31	Piazzola T3_13	10 days	30	Tue 14/06/22	[Timeline bar from Jan 2022 to Jan 2022]									
32	Strada T3_14	10 days	31	Tue 28/06/22	[Timeline bar from Jan 2022 to Jan 2022]									
33	Piazzola T3_14	10 days	32	Tue 12/07/22	[Timeline bar from Jan 2022 to Jan 2022]									
34	Strada T3_15	10 days	33	Tue 26/07/22	[Timeline bar from Jan 2022 to Jan 2022]									
35	Piazzola T3_15	10 days	34	Tue 09/08/22	[Timeline bar from Jan 2022 to Jan 2022]									
36	Strada T3_16	10 days	35	Tue 23/08/22	[Timeline bar from Jan 2022 to Jan 2022]									
37	Piazzola T3_16	10 days	36	Tue 06/09/22	[Timeline bar from Jan 2022 to Jan 2022]									
38	Strada T3_17	10 days	37	Tue 20/09/22	[Timeline bar from Jan 2022 to Jan 2022]									
39	Piazzola T3_17	10 days	38	Tue 04/10/22	[Timeline bar from Jan 2022 to Jan 2022]									
40	Strada T3_18	10 days	39	Tue 18/10/22	[Timeline bar from Jan 2022 to Jan 2022]									
41	Piazzola T3_18	10 days	40	Tue 01/11/22	[Timeline bar from Jan 2022 to Jan 2022]									
42	Strada T3_19	10 days	41	Tue 15/11/22	[Timeline bar from Jan 2022 to Jan 2022]									
43	Piazzola T3_19	10 days	42	Tue 29/11/22	[Timeline bar from Jan 2022 to Jan 2022]									
44	Strada T3_20	10 days	43	Tue 13/12/22	[Timeline bar from Jan 2022 to Jan 2022]									
45	Piazzola T3_20	10 days	44	Tue 27/12/22	[Timeline bar from Jan 2022 to Jan 2022]									
46	Strada T3_21	10 days	4FS-10 days	Tue 05/04/22	[Timeline bar from Jan 2022 to Jan 2022]									
47	Piazzola T3_21	10 days	46	Tue 19/04/22	[Timeline bar from Jan 2022 to Jan 2022]									

Project: Cronoprogramma Date: Fri 11/12/20	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Slippage	
	Summary		Inactive Task		Duration-only		Finish-only			

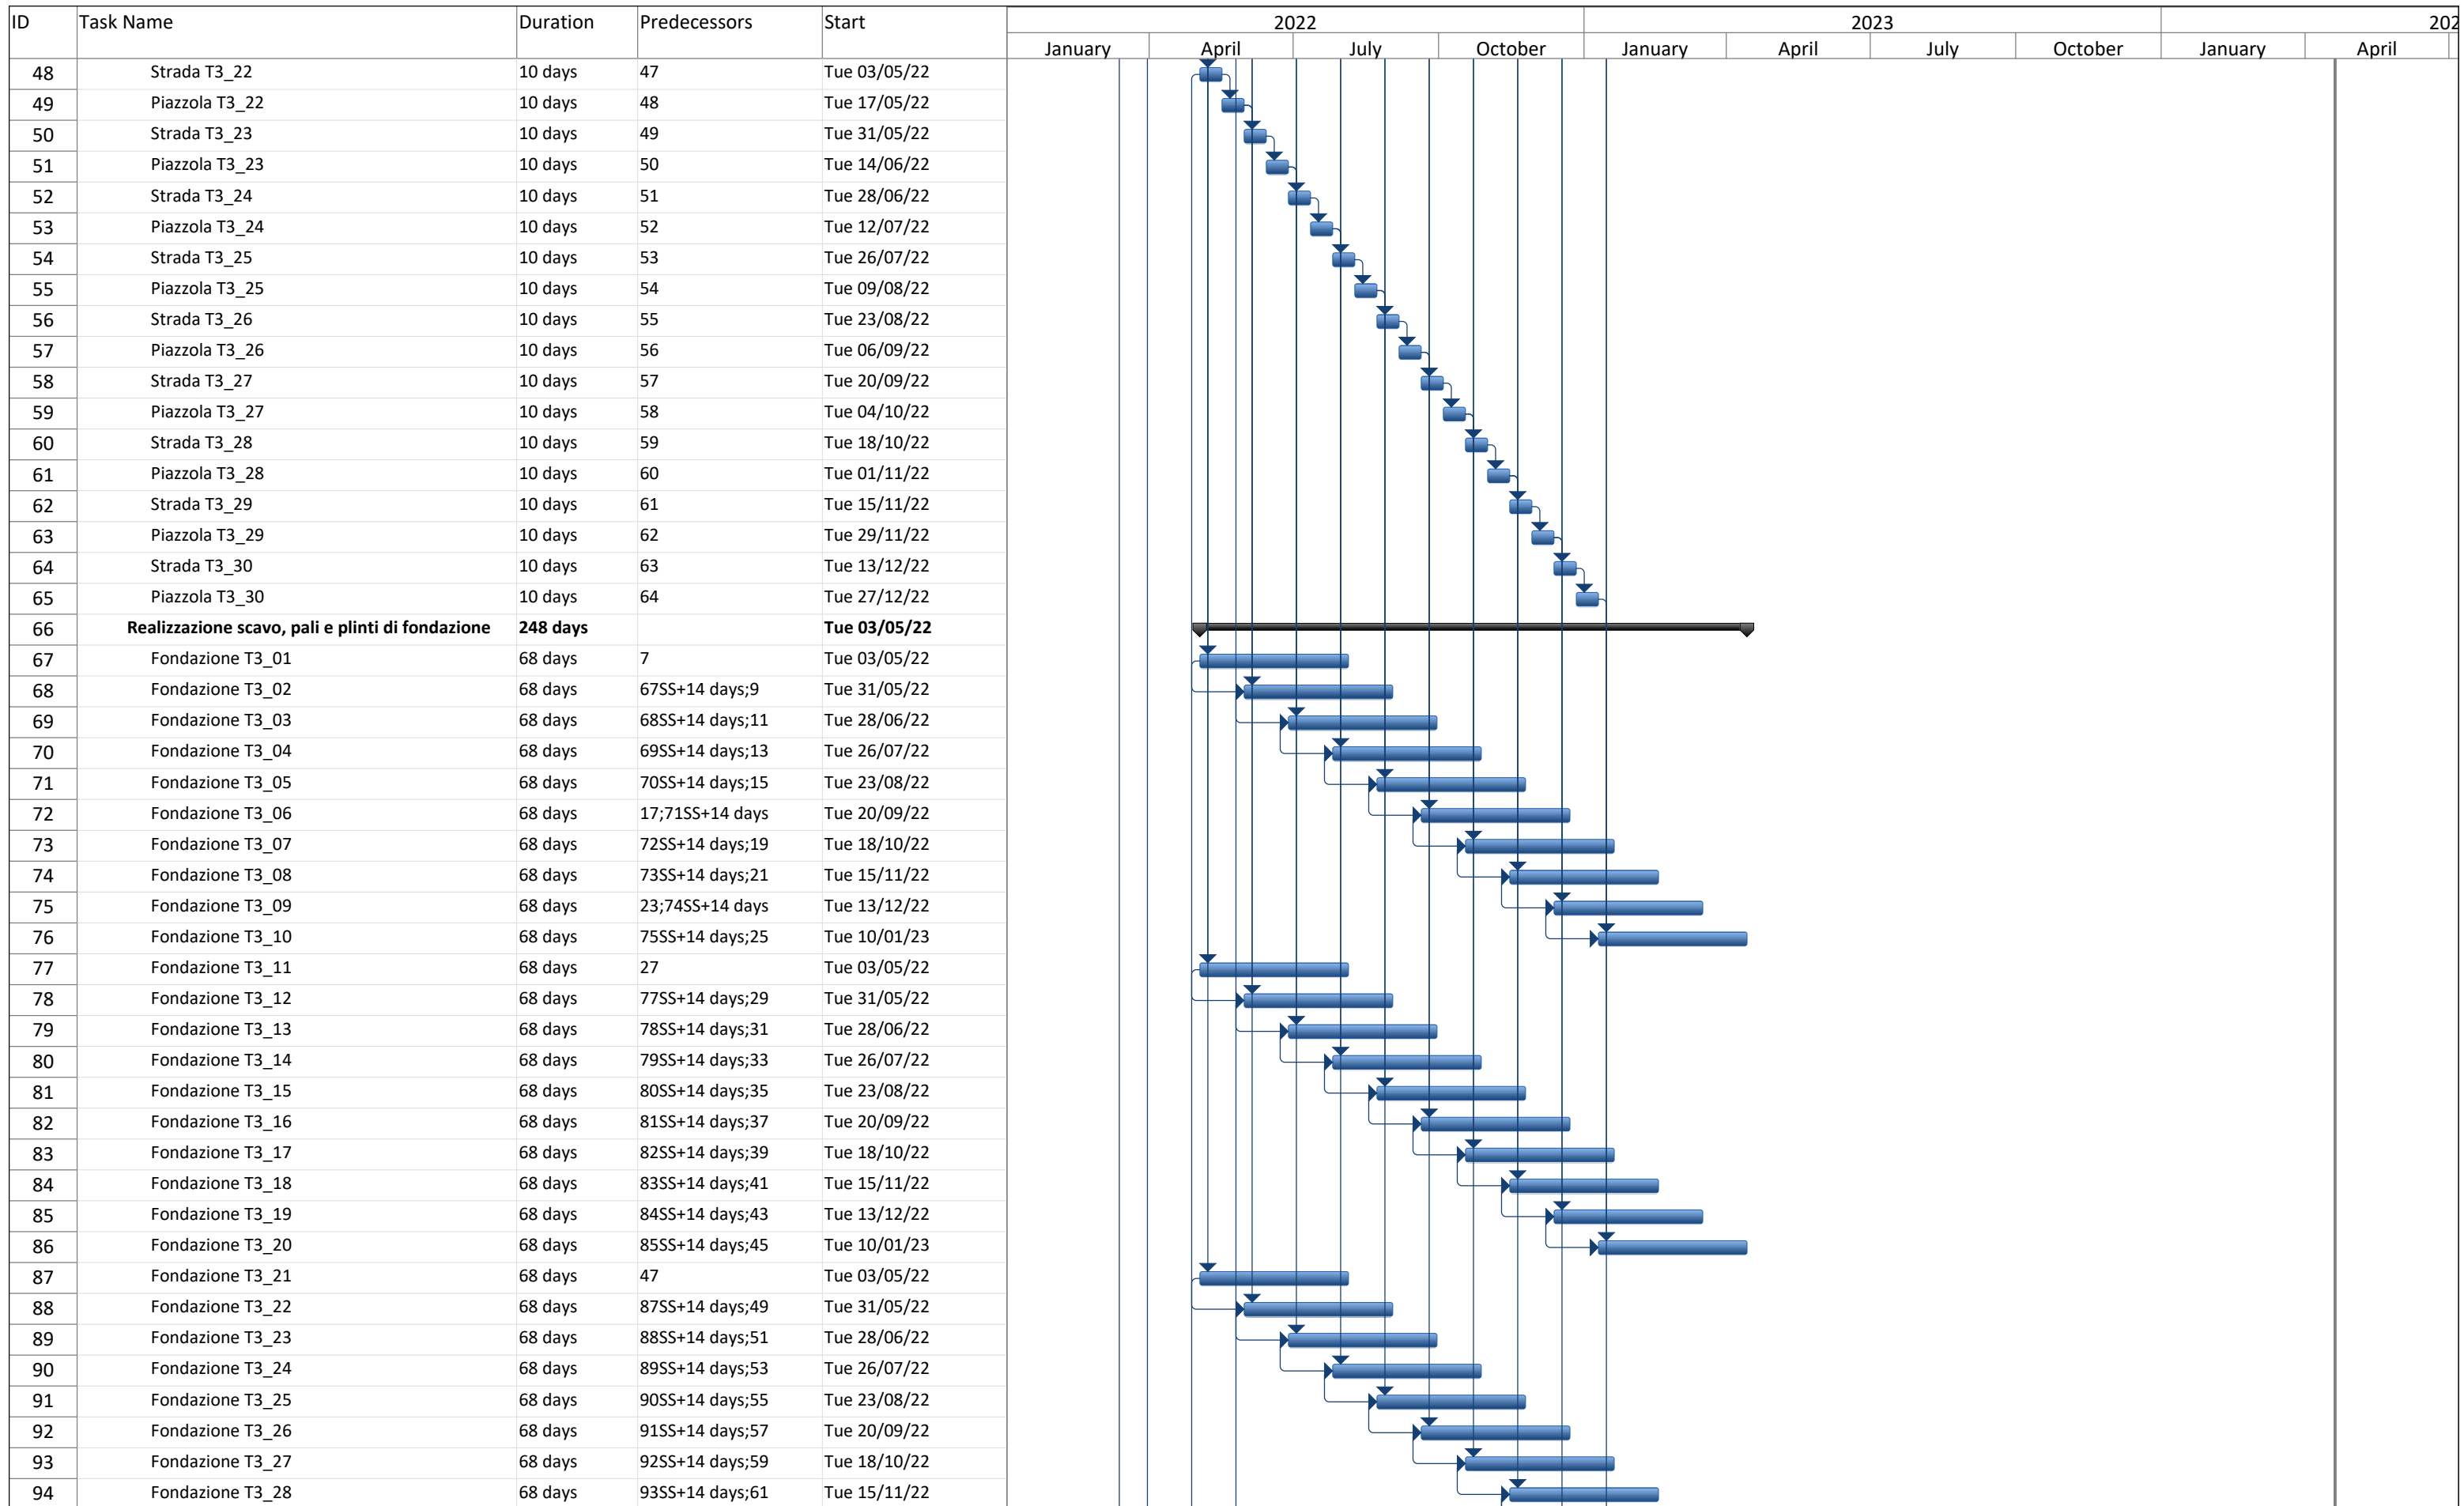

Project: Cronoprogramma  
Date: Fri 11/12/20


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Slippage	
Summary		Inactive Task		Duration-only		Finish-only			

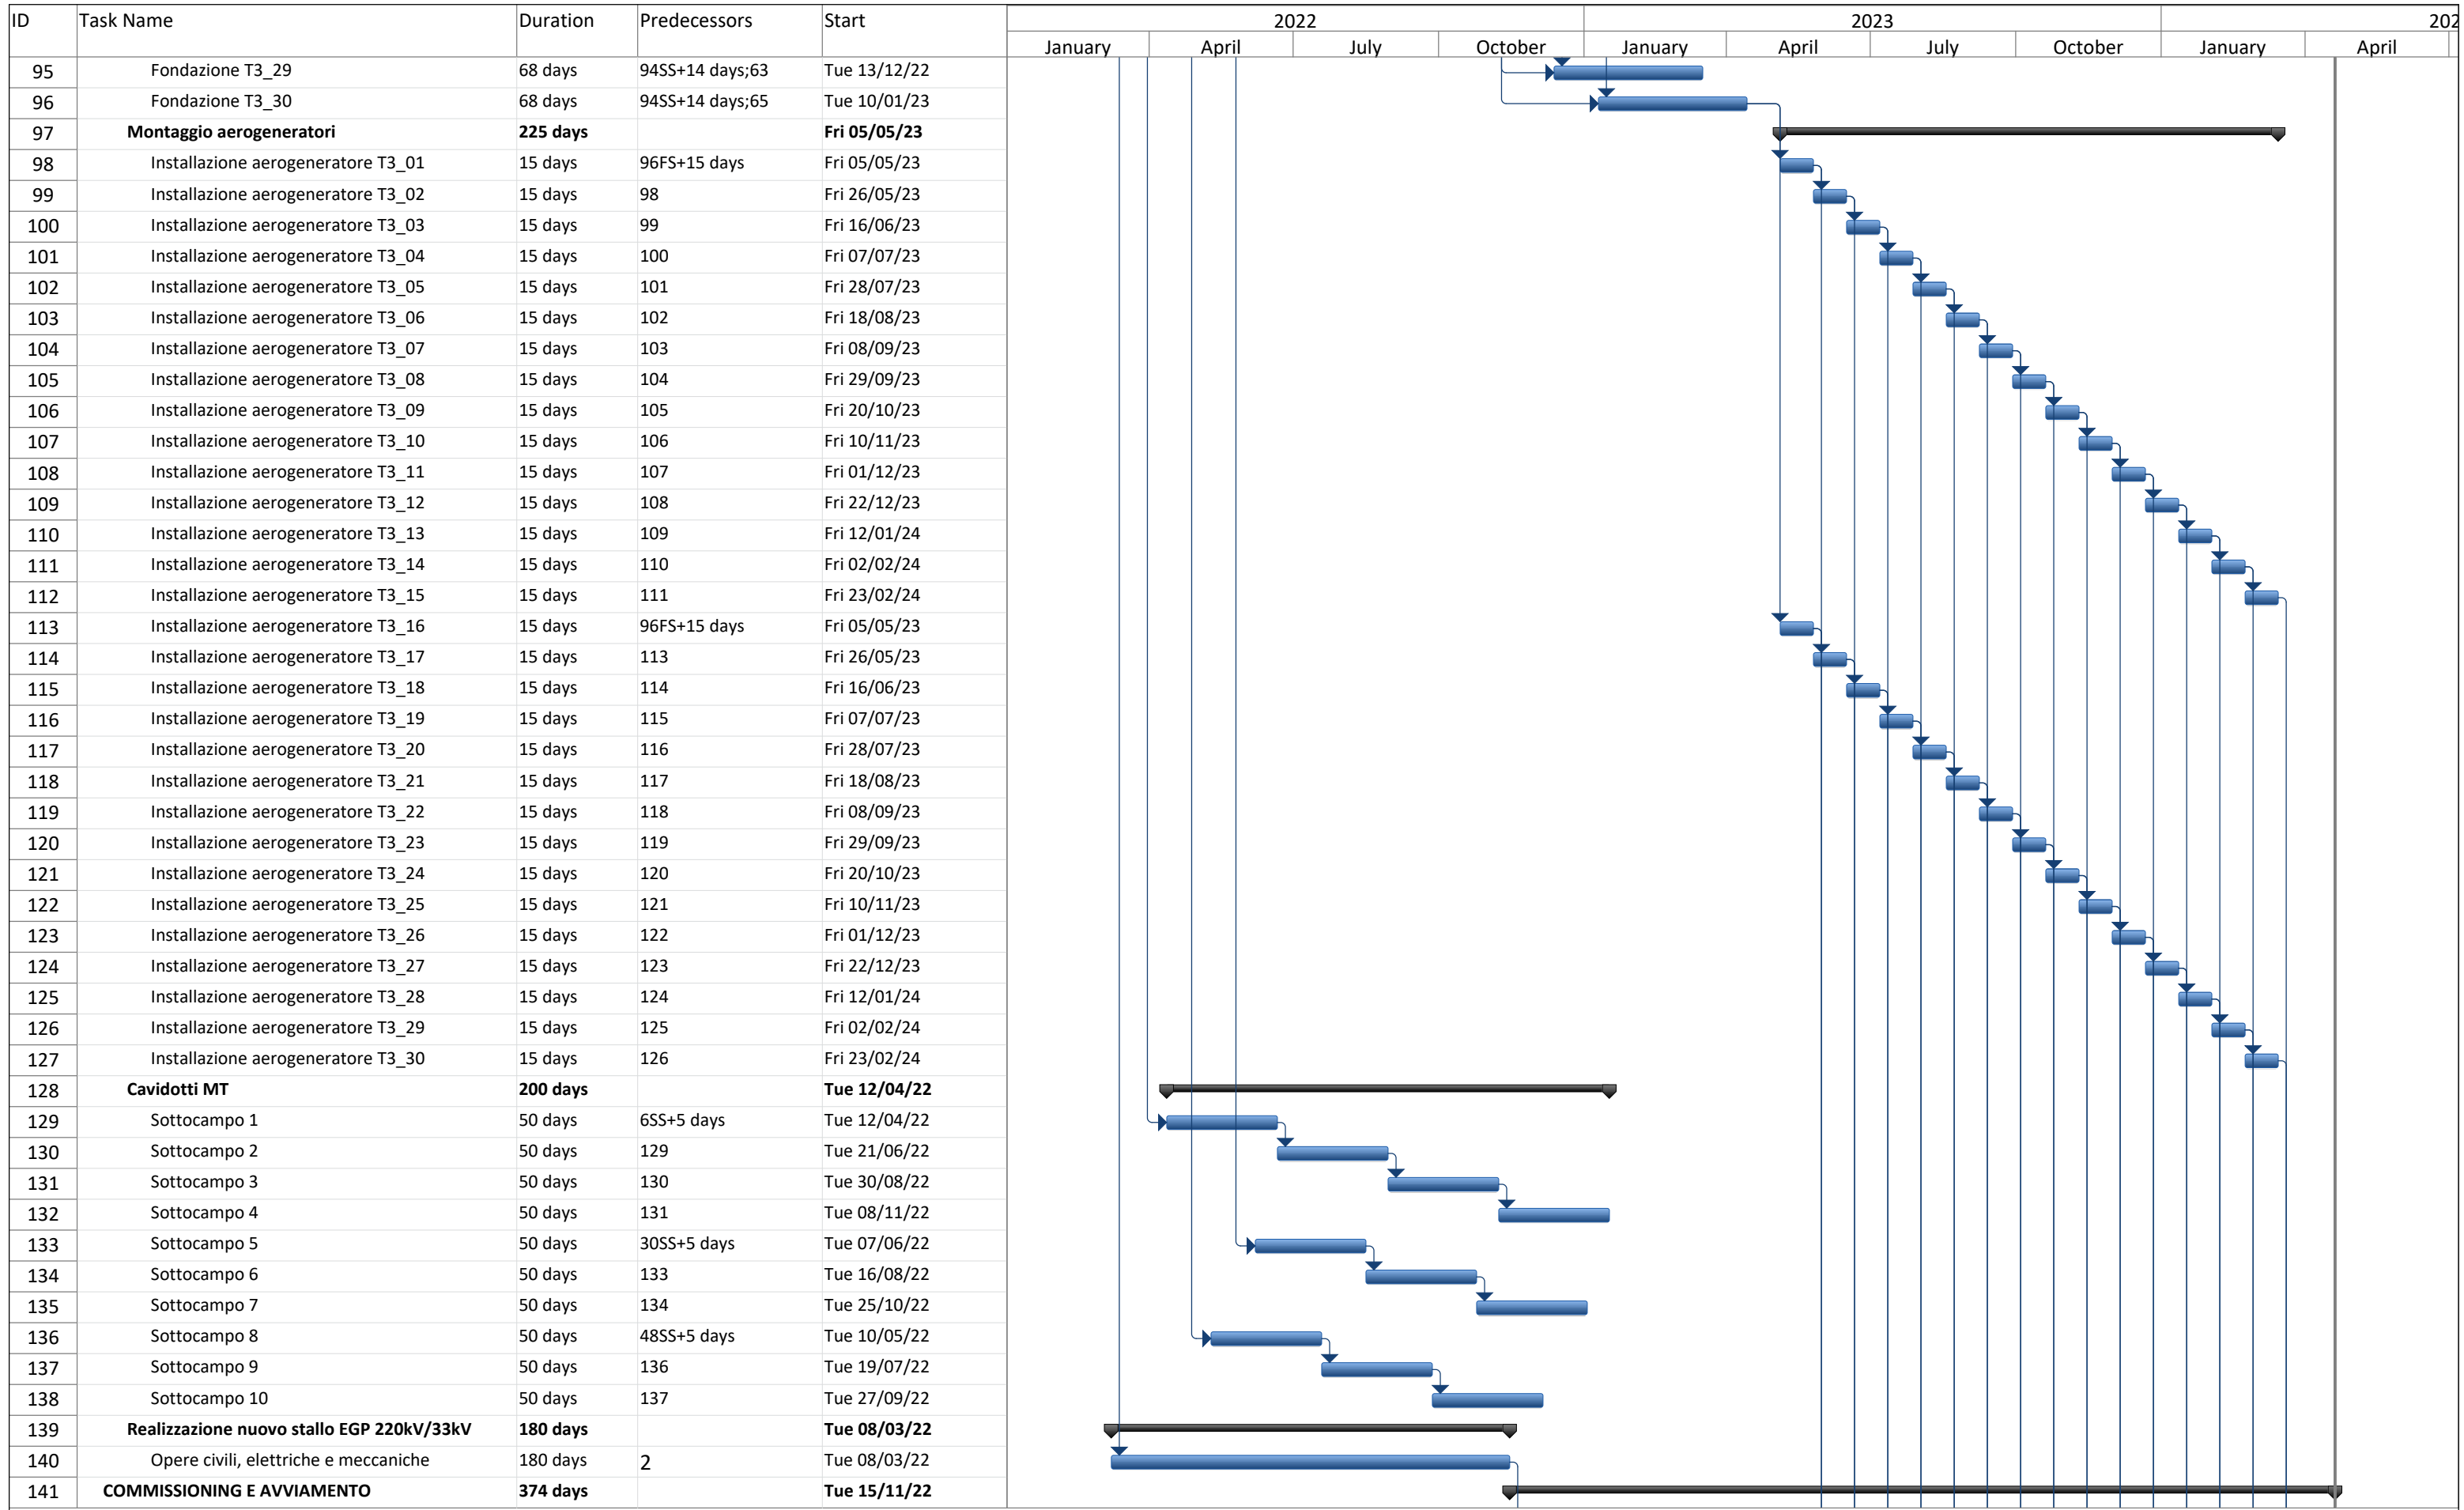

Project: Cronoprogramma  
Date: Fri 11/12/20

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Slippage	
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Predecessors	Start	2022				2023				2024	
					January	April	July	October	January	April	July	October	January	April
142	<b>Commissioning</b>	<b>369 days</b>		<b>Tue 15/11/22</b>										
143	Commissioning T3_01	21 days	98;173	Fri 26/05/23										
144	Commissioning T3_02	21 days	99;143SS+14 days	Fri 16/06/23										
145	Commissioning T3_03	21 days	100;144SS+14 days	Fri 07/07/23										
146	Commissioning T3_04	21 days	101;145SS+14 days	Fri 28/07/23										
147	Commissioning T3_05	21 days	146SS+14 days;102	Fri 18/08/23										
148	Commissioning T3_06	21 days	147SS+14 days;103	Fri 08/09/23										
149	Commissioning T3_07	21 days	148SS+14 days;104	Fri 29/09/23										
150	Commissioning T3_08	21 days	149SS+14 days;105	Fri 20/10/23										
151	Commissioning T3_09	21 days	150SS+14 days;106	Fri 10/11/23										
152	Commissioning T3_10	21 days	151SS+14 days;107	Fri 01/12/23										
153	Commissioning T3_11	21 days	152SS+14 days;108	Fri 22/12/23										
154	Commissioning T3_12	21 days	153SS+14 days;109	Fri 12/01/24										
155	Commissioning T3_13	21 days	154SS+14 days;110	Fri 02/02/24										
156	Commissioning T3_14	21 days	155SS+14 days;111	Fri 23/02/24										
157	Commissioning T3_15	21 days	156SS+14 days;112	Fri 15/03/24										
158	Commissioning T3_16	21 days	113	Fri 26/05/23										
159	Commissioning T3_17	21 days	158SS+14 days;114	Fri 16/06/23										
160	Commissioning T3_18	21 days	159SS+14 days;115	Fri 07/07/23										
161	Commissioning T3_19	21 days	160SS+14 days;116	Fri 28/07/23										
162	Commissioning T3_20	21 days	161SS+14 days;117	Fri 18/08/23										
163	Commissioning T3_21	21 days	162SS+14 days;118	Fri 08/09/23										
164	Commissioning T3_22	21 days	163SS+14 days;119	Fri 29/09/23										
165	Commissioning T3_23	21 days	164SS+14 days;120	Fri 20/10/23										
166	Commissioning T3_24	21 days	165SS+14 days;121	Fri 10/11/23										
167	Commissioning T3_25	21 days	166SS+14 days;122	Fri 01/12/23										
168	Commissioning T3_26	21 days	167SS+14 days;123	Fri 22/12/23										
169	Commissioning T3_27	21 days	168SS+14 days;124	Fri 12/01/24										
170	Commissioning T3_28	21 days	169SS+14 days;125	Fri 02/02/24										
171	Commissioning T3_29	21 days	170SS+14 days;126	Fri 23/02/24										
172	Commissioning T3_30	21 days	171SS+14 days;127	Fri 15/03/24										
173	Commissioning SSE	15 days	140	Tue 15/11/22										
174	1° parallelo con rete elettrica	0 days	142	Fri 12/04/24										
175	Avviamento	5 days	174	Mon 15/04/24										
176	Entrata in esercizio - COD	0 days	175	Fri 19/04/24										

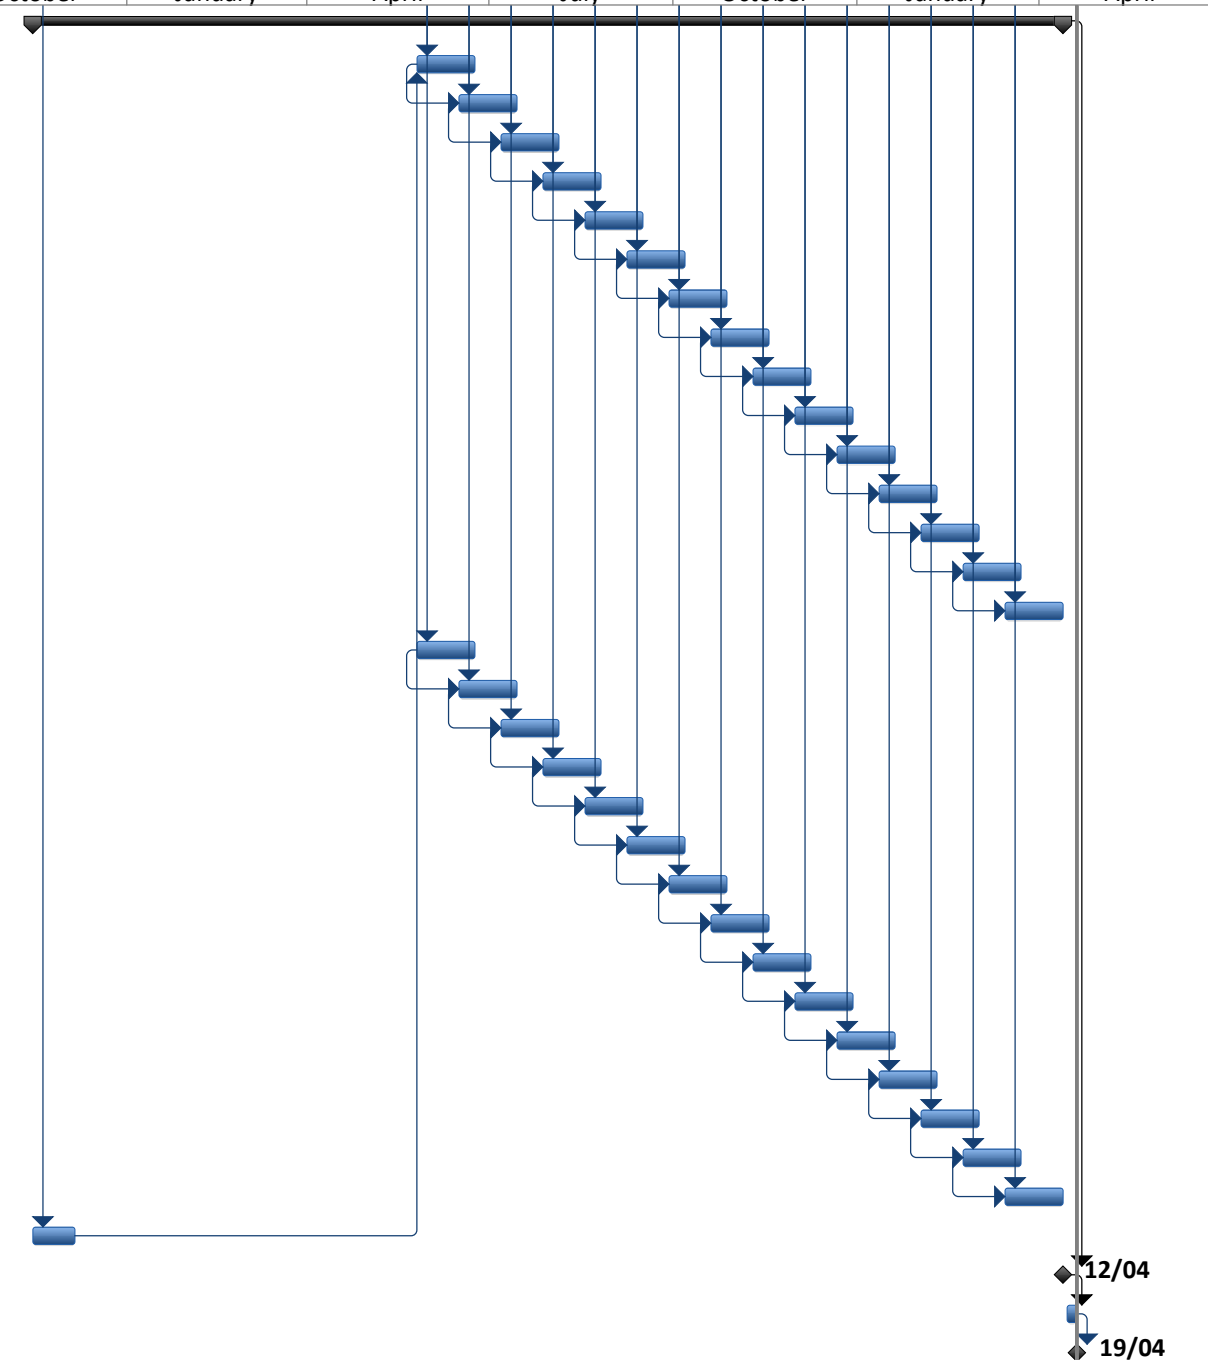

Project: Cronoprogramma Date: Fri 11/12/20	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Slippage	
	Summary		Inactive Task		Duration-only		Finish-only			
