



Green Power

Engineering & Construction



GRE CODE

GRE.EEC.P.73.IT.W.12420.00.019.00

PAGE

1 di/of 3

TITLE:

AVAILABLE LANGUAGE: IT

INTEGRALE RICOSTRUZIONE DELL'IMPIANTO EOLICO DI NICOSIA

PROGETTO DEFINITIVO

Cronoprogramma



File: GRE.EEC.P.73.IT.W.12420.00.019.00 - Cronoprogramma.docx

REV.	DATE	DESCRIPTION	PREPARED	VERIFIED	APPROVED
00	03/07/2020	Prima emissione	M.Terzi	N.Novati	L.Lavazza

GRE VALIDATION

-	-	laciofano
COLLABORATORS	VERIFIED BY	VALIDATED BY

PROJECT / PLANT Nicosia	GRE CODE																			
	GROUP	FUNCTION	TYPE	ISSUER	COUNTRY	TEC	PLANT				SYSTEM	PROGRESSIVE	REVISION							
	GRE	EEC	P	7	3	I	T	W	1	2	4	2	0	0	0	0	1	9	0	0
CLASSIFICATION	PUBLIC					UTILIZATION SCOPE	BASIC DESIGN													

This document is property of Enel Green Power S.p.A. It is strictly forbidden to reproduce this document, in whole or in part, and to provide to others any related information without the previous written consent by Enel Green Power S.p.A.



Green Power

Engineering & Construction



GRE CODE


GRE.EEC.P.73.IT.W.12420.00.019.00

PAGE

2 di/of 3

INDEX

1. CRONOPROGRAMMA.....**3**

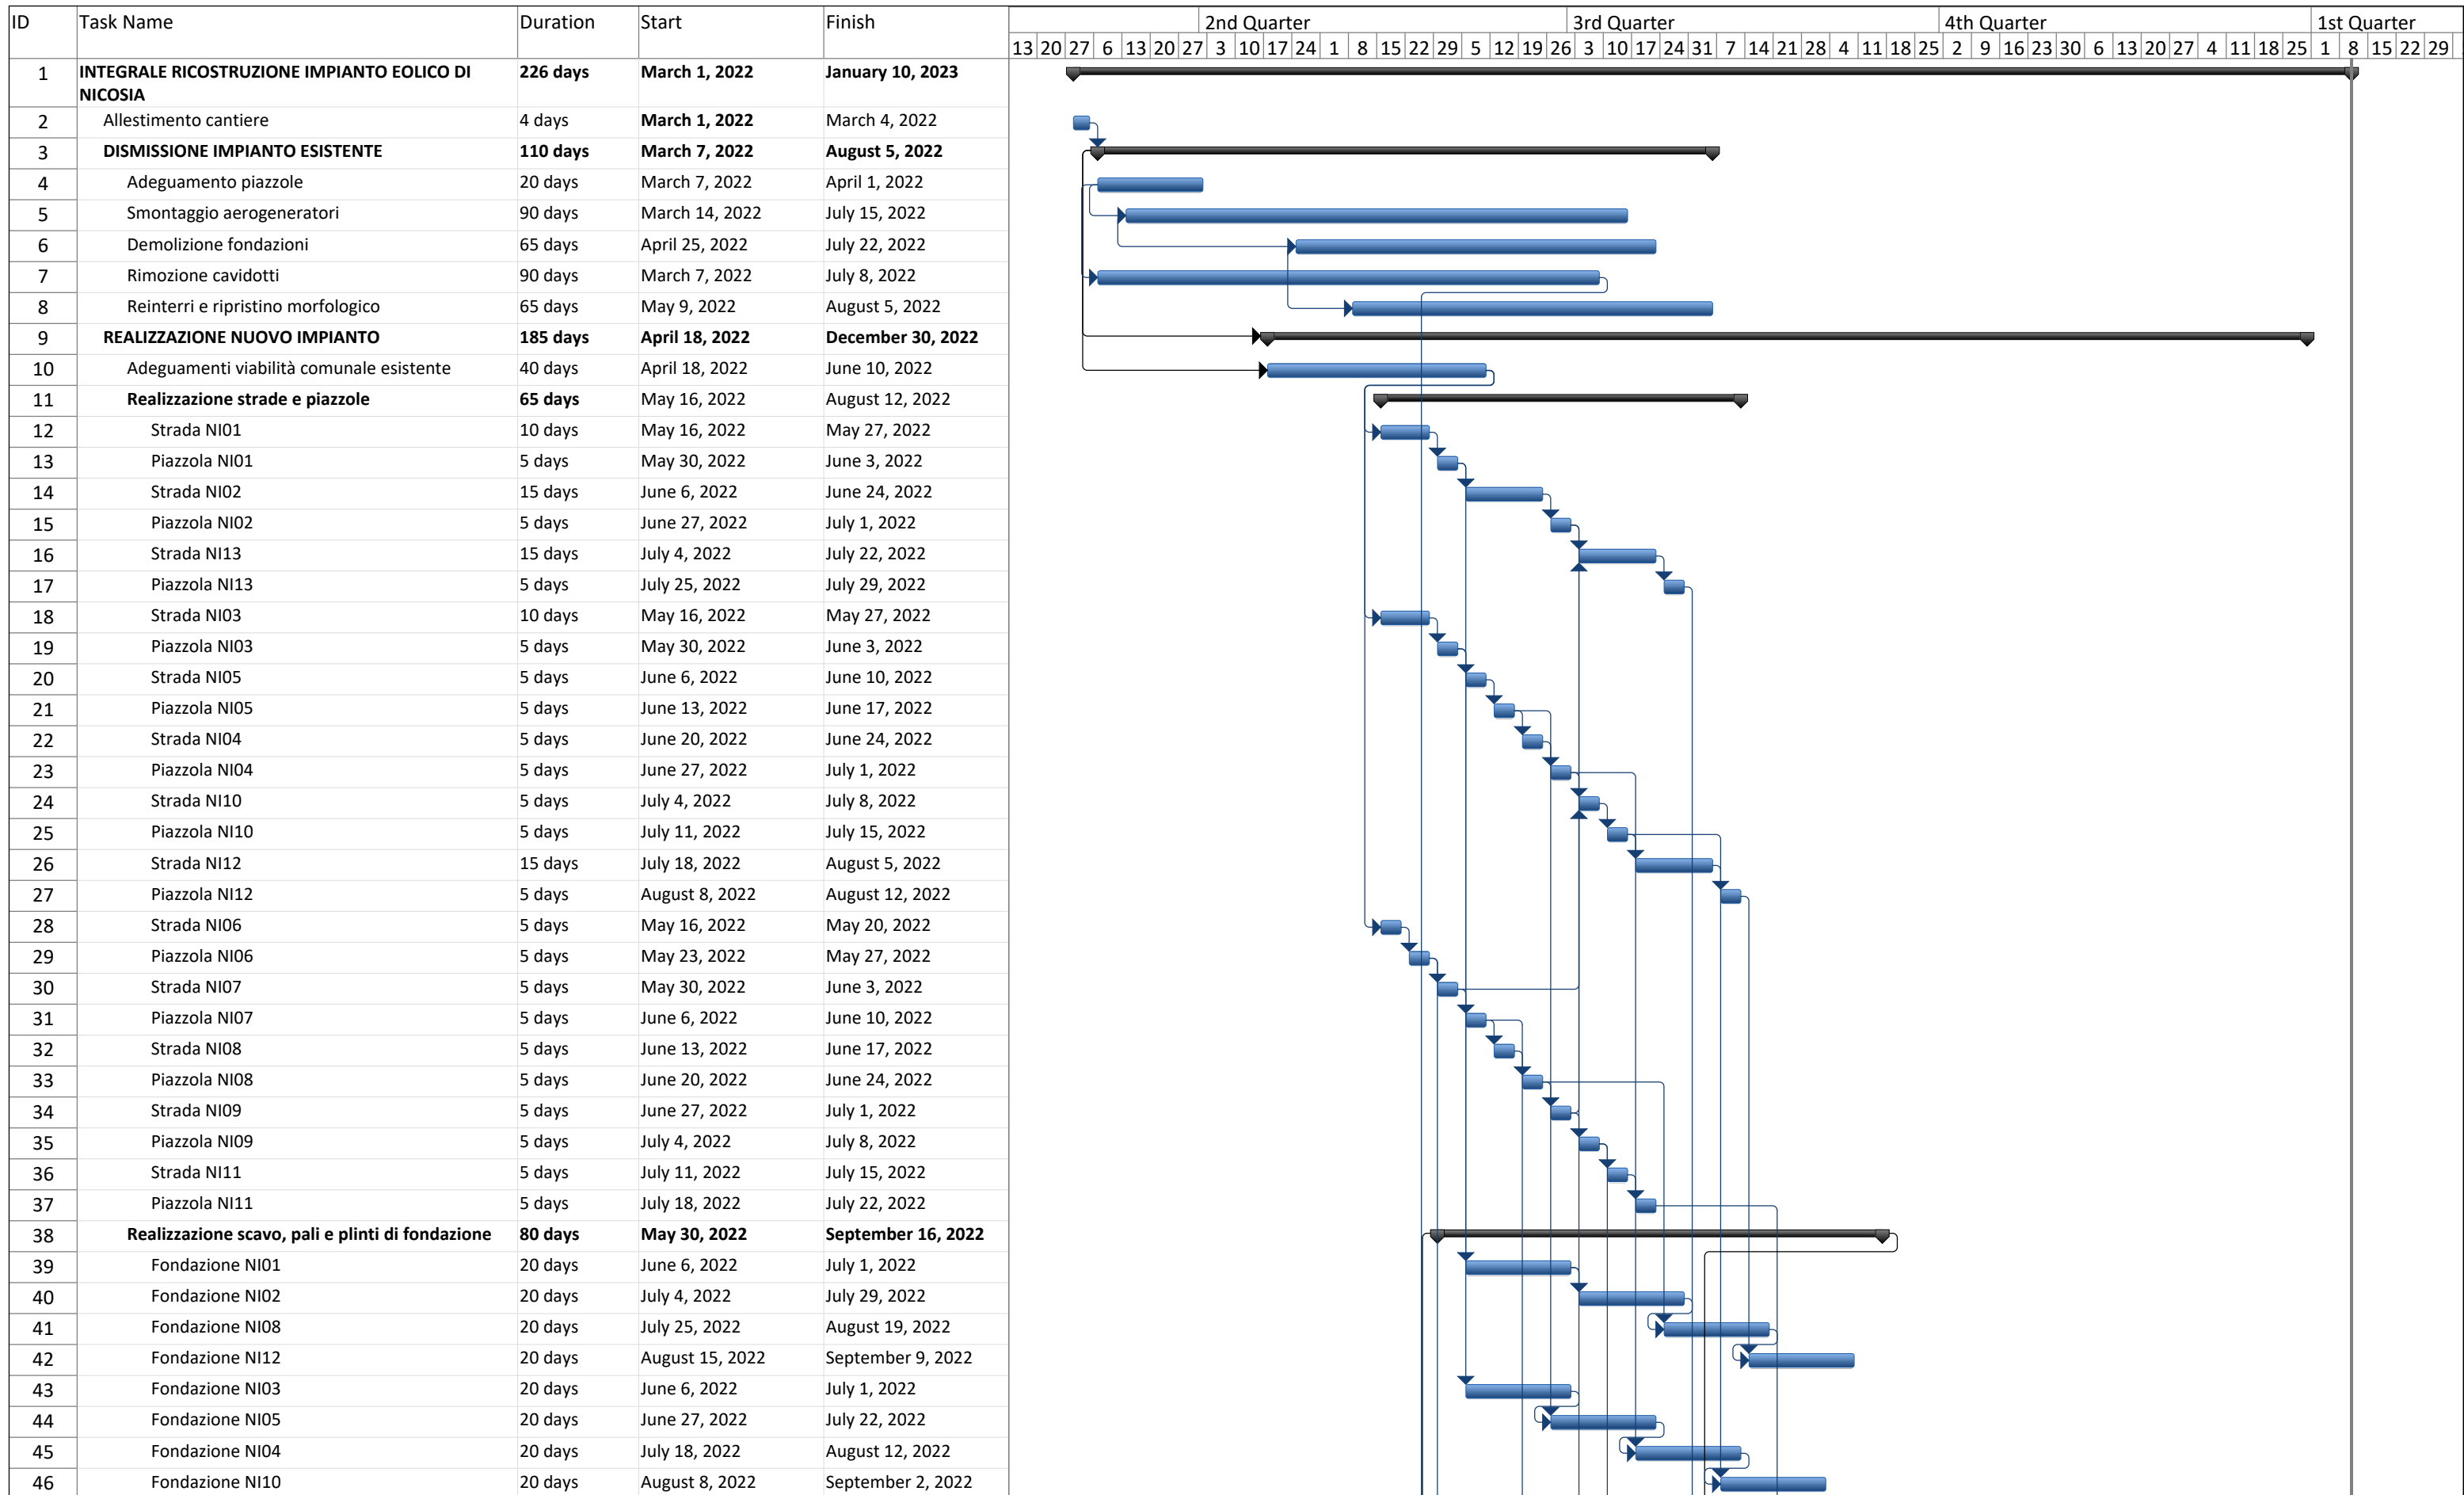

Project: Project2 Date: July 2, 2020	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Slippage	
	Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	2nd Quarter										3rd Quarter										4th Quarter										1st Quarter															
					13	20	27	6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7	14	21	28	4	11	18	25	2	9	16	23	30	6	13	20	27	4	11	18	25
47	Fondazione NI06	20 days	May 30, 2022	June 24, 2022																																														
48	Fondazione NI07	20 days	June 20, 2022	July 15, 2022																																														
49	Fondazione NI09	20 days	July 11, 2022	August 5, 2022																																														
50	Fondazione NI13	20 days	August 1, 2022	August 26, 2022																																														
51	Fondazione NI11	20 days	August 22, 2022	September 16, 2022																																														
52	Montaggio aerogeneratori	130 days	July 4, 2022	December 30, 2022																																														
53	Installazione aerogeneratore NI01	10 days	July 4, 2022	July 15, 2022																																														
54	Installazione aerogeneratore NI02	10 days	July 18, 2022	July 29, 2022																																														
55	Installazione aerogeneratore NI03	10 days	August 1, 2022	August 12, 2022																																														
56	Installazione aerogeneratore NI04	10 days	August 15, 2022	August 26, 2022																																														
57	Installazione aerogeneratore NI05	10 days	August 29, 2022	September 9, 2022																																														
58	Installazione aerogeneratore NI06	10 days	September 12, 2022	September 23, 2022																																														
59	Installazione aerogeneratore NI07	10 days	September 26, 2022	October 7, 2022																																														
60	Installazione aerogeneratore NI08	10 days	October 10, 2022	October 21, 2022																																														
61	Installazione aerogeneratore NI09	10 days	October 24, 2022	November 4, 2022																																														
62	Installazione aerogeneratore NI10	10 days	November 7, 2022	November 18, 2022																																														
63	Installazione aerogeneratore NI11	10 days	November 21, 2022	December 2, 2022																																														
64	Installazione aerogeneratore NI12	10 days	December 5, 2022	December 16, 2022																																														
65	Installazione aerogeneratore NI13	10 days	December 19, 2022	December 30, 2022																																														
66	Posa cavidotti interrati 33 kV	38 days	May 30, 2022	July 20, 2022																																														
67	Sottocampo 5	10 days	May 30, 2022	June 10, 2022																																														
68	Sottocampo 4	20 days	June 13, 2022	July 8, 2022																																														
69	Sottocampo 3	15 days	June 20, 2022	July 8, 2022																																														
70	Sottocampo 2	15 days	June 27, 2022	July 15, 2022																																														
71	Sottocampo 1	13 days	July 4, 2022	July 20, 2022																																														
72	Adeguamento SSE 150kV/33kV	10 days	July 28, 2022	August 10, 2022																																														
73	Reinterrati e ripristino morfologico	40 days	August 8, 2022	September 30, 2022																																														
74	COMMISSIONING E AVVIAMENTO	67 days	October 10, 2022	January 10, 2023																																														
75	Commissioning	62 days	October 10, 2022	January 3, 2023																																														
76	Commissioning NI01	2 days	October 10, 2022	October 11, 2022																																														
77	Commissioning NI02	2 days	October 10, 2022	October 11, 2022																																														
78	Commissioning NI03	2 days	October 10, 2022	October 11, 2022																																														
79	Commissioning NI04	2 days	October 10, 2022	October 11, 2022																																														
80	Commissioning NI05	2 days	October 10, 2022	October 11, 2022																																														
81	Commissioning NI06	2 days	October 10, 2022	October 11, 2022																																														
82	Commissioning NI07	2 days	October 10, 2022	October 11, 2022																																														
83	Commissioning NI08	2 days	October 24, 2022	October 25, 2022																																														
84	Commissioning NI09	2 days	November 7, 2022	November 8, 2022																																														
85	Commissioning NI10	2 days	November 21, 2022	November 22, 2022																																														
86	Commissioning NI11	2 days	December 5, 2022	December 6, 2022																																														
87	Commissioning NI12	2 days	December 19, 2022	December 20, 2022																																														
88	Commissioning NI13	2 days	January 2, 2023	January 3, 2023																																														
89	1° parallelo con rete elettrica	0 days	January 3, 2023	January 3, 2023																																														
90	Avviamento	5 days	January 4, 2023	January 10, 2023																																														
91	Entrata in esercizio - COD	0 days	January 10, 2023	January 10, 2023																																														

Project: Project2 Date: July 2, 2020	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Slippage	
	Summary		Inactive Task		Duration-only		Finish-only			
