

TITLE:

AVAILABLE LANGUAGE: IT

IMPIANTO EOLICO "CALTAVUTURO ESTENSIONE"

PROGETTO DEFINITIVO

Cronoprogramma

File: GRE.EEC.P.73.IT.W.14362.00.014.00 - Cronoprogramma

REV.	DATE	DESCRIPTION	PREPARED	VERIFIED	APPROVED
00	12/02/2021	Prima emissione	N. Novati	D. Gradogna	P. Polinelli

GRE VALIDATION

	<i>Iaciofano</i>	<i>Iaciofano</i>
COLLABORATORS	VERIFIED BY	VALIDATED BY


PROJECT / PLANT Caltavuturo Estensione	GRE CODE																		
	GROUP	FUNCION	TYPE	ISSUER	COUNTRY	TEC	PLANT				SYSTEM	PROGRESSIVE	REVISION						
	GRE	EEC	P	7	3	I	T	W	1	4	3	6	2	0	0	0	1	4	0

CLASSIFICATION	PUBLIC	UTILIZATION SCOPE	BASIC DESIGN
----------------	---------------	-------------------	---------------------

ID	Task Name	Duration	Start	Finish	2022				2023				20	
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4		Qtr 1
1	IMPIANTO EOLICO CALTAVUTURO ESTENSIONE	525 days	Tue 01/03/22	Mon 04/03/24										
2	Allestimento cantiere	5 days	Tue 01/03/22	Mon 07/03/22										
3	REALIZZAZIONE NUOVO IMPIANTO	493 days	Tue 08/03/22	Thu 25/01/24										
4	Adeguamenti viabilità esistente	30 days	Tue 08/03/22	Mon 18/04/22										
5	Realizzazione strade e piazzole	120 days	Tue 05/04/22	Mon 19/09/22										
6	Strada CTV_E01	10 days	Tue 05/04/22	Mon 18/04/22										
7	Piazzola CTV_E01	10 days	Tue 19/04/22	Mon 02/05/22										
8	Strada CTV_E02	10 days	Tue 03/05/22	Mon 16/05/22										
9	Piazzola CTV_E02	10 days	Tue 17/05/22	Mon 30/05/22										
10	Strada CTV_E03	10 days	Tue 31/05/22	Mon 13/06/22										
11	Piazzola CTV_E03	10 days	Tue 14/06/22	Mon 27/06/22										
12	Strada CTV_E04	10 days	Tue 28/06/22	Mon 11/07/22										
13	Piazzola CTV_E04	10 days	Tue 12/07/22	Mon 25/07/22										
14	Strada CTV_E05	10 days	Tue 26/07/22	Mon 08/08/22										
15	Piazzola CTV_E05	10 days	Tue 09/08/22	Mon 22/08/22										
16	Strada CTV_E06	10 days	Tue 23/08/22	Mon 05/09/22										
17	Piazzola CTV_E06	10 days	Tue 06/09/22	Mon 19/09/22										
18	Strada CTV_E07	10 days	Tue 05/04/22	Mon 18/04/22										
19	Piazzola CTV_E07	10 days	Tue 19/04/22	Mon 02/05/22										
20	Strada CTV_E08	10 days	Tue 03/05/22	Mon 16/05/22										
21	Piazzola CTV_E08	10 days	Tue 17/05/22	Mon 30/05/22										
22	Strada CTV_E09	10 days	Tue 31/05/22	Mon 13/06/22										
23	Piazzola CTV_E09	10 days	Tue 14/06/22	Mon 27/06/22										
24	Strada CTV_E10	10 days	Tue 28/06/22	Mon 11/07/22										
25	Piazzola CTV_E10	10 days	Tue 12/07/22	Mon 25/07/22										
26	Strada CTV_E11	10 days	Tue 26/07/22	Mon 08/08/22										
27	Piazzola CTV_E11	10 days	Tue 09/08/22	Mon 22/08/22										
28	Strada CTV_E12	10 days	Tue 23/08/22	Mon 05/09/22										
29	Piazzola CTV_E12	10 days	Tue 06/09/22	Mon 19/09/22										
30	Strada CTV_E13	10 days	Tue 05/04/22	Mon 18/04/22										
31	Piazzola CTV_E13	10 days	Tue 19/04/22	Mon 02/05/22										
32	Strada CTV_E14	10 days	Tue 03/05/22	Mon 16/05/22										
33	Piazzola CTV_E14	10 days	Tue 17/05/22	Mon 30/05/22										
34	Strada CTV_E15	10 days	Tue 31/05/22	Mon 13/06/22										
35	Piazzola CTV_E15	10 days	Tue 14/06/22	Mon 27/06/22										
36	Strada CTV_E16	10 days	Tue 28/06/22	Mon 11/07/22										
37	Piazzola CTV_E16	10 days	Tue 12/07/22	Mon 25/07/22										
38	Strada CTV_E17	10 days	Tue 26/07/22	Mon 08/08/22										
39	Piazzola CTV_E17	10 days	Tue 09/08/22	Mon 22/08/22										
40	Strada CTV_E18	10 days	Tue 23/08/22	Mon 05/09/22										
41	Piazzola CTV_E18	10 days	Tue 06/09/22	Mon 19/09/22										
42	Realizzazione scavo, pali e plinti di fondazione	168 days	Tue 03/05/22	Thu 22/12/22										
43	Fondazione CTV_E01	68 days	Tue 03/05/22	Thu 04/08/22										
44	Fondazione CTV_E02	68 days	Tue 31/05/22	Thu 01/09/22										
45	Fondazione CTV_E03	68 days	Tue 28/06/22	Thu 29/09/22										
46	Fondazione CTV_E04	68 days	Tue 26/07/22	Thu 27/10/22										
47	Fondazione CTV_E05	68 days	Tue 23/08/22	Thu 24/11/22										

Project: Cronoprogramma
Date: Mon 01/02/21

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Slippage	
Summary		Inactive Task		Duration-only		Finish-only			

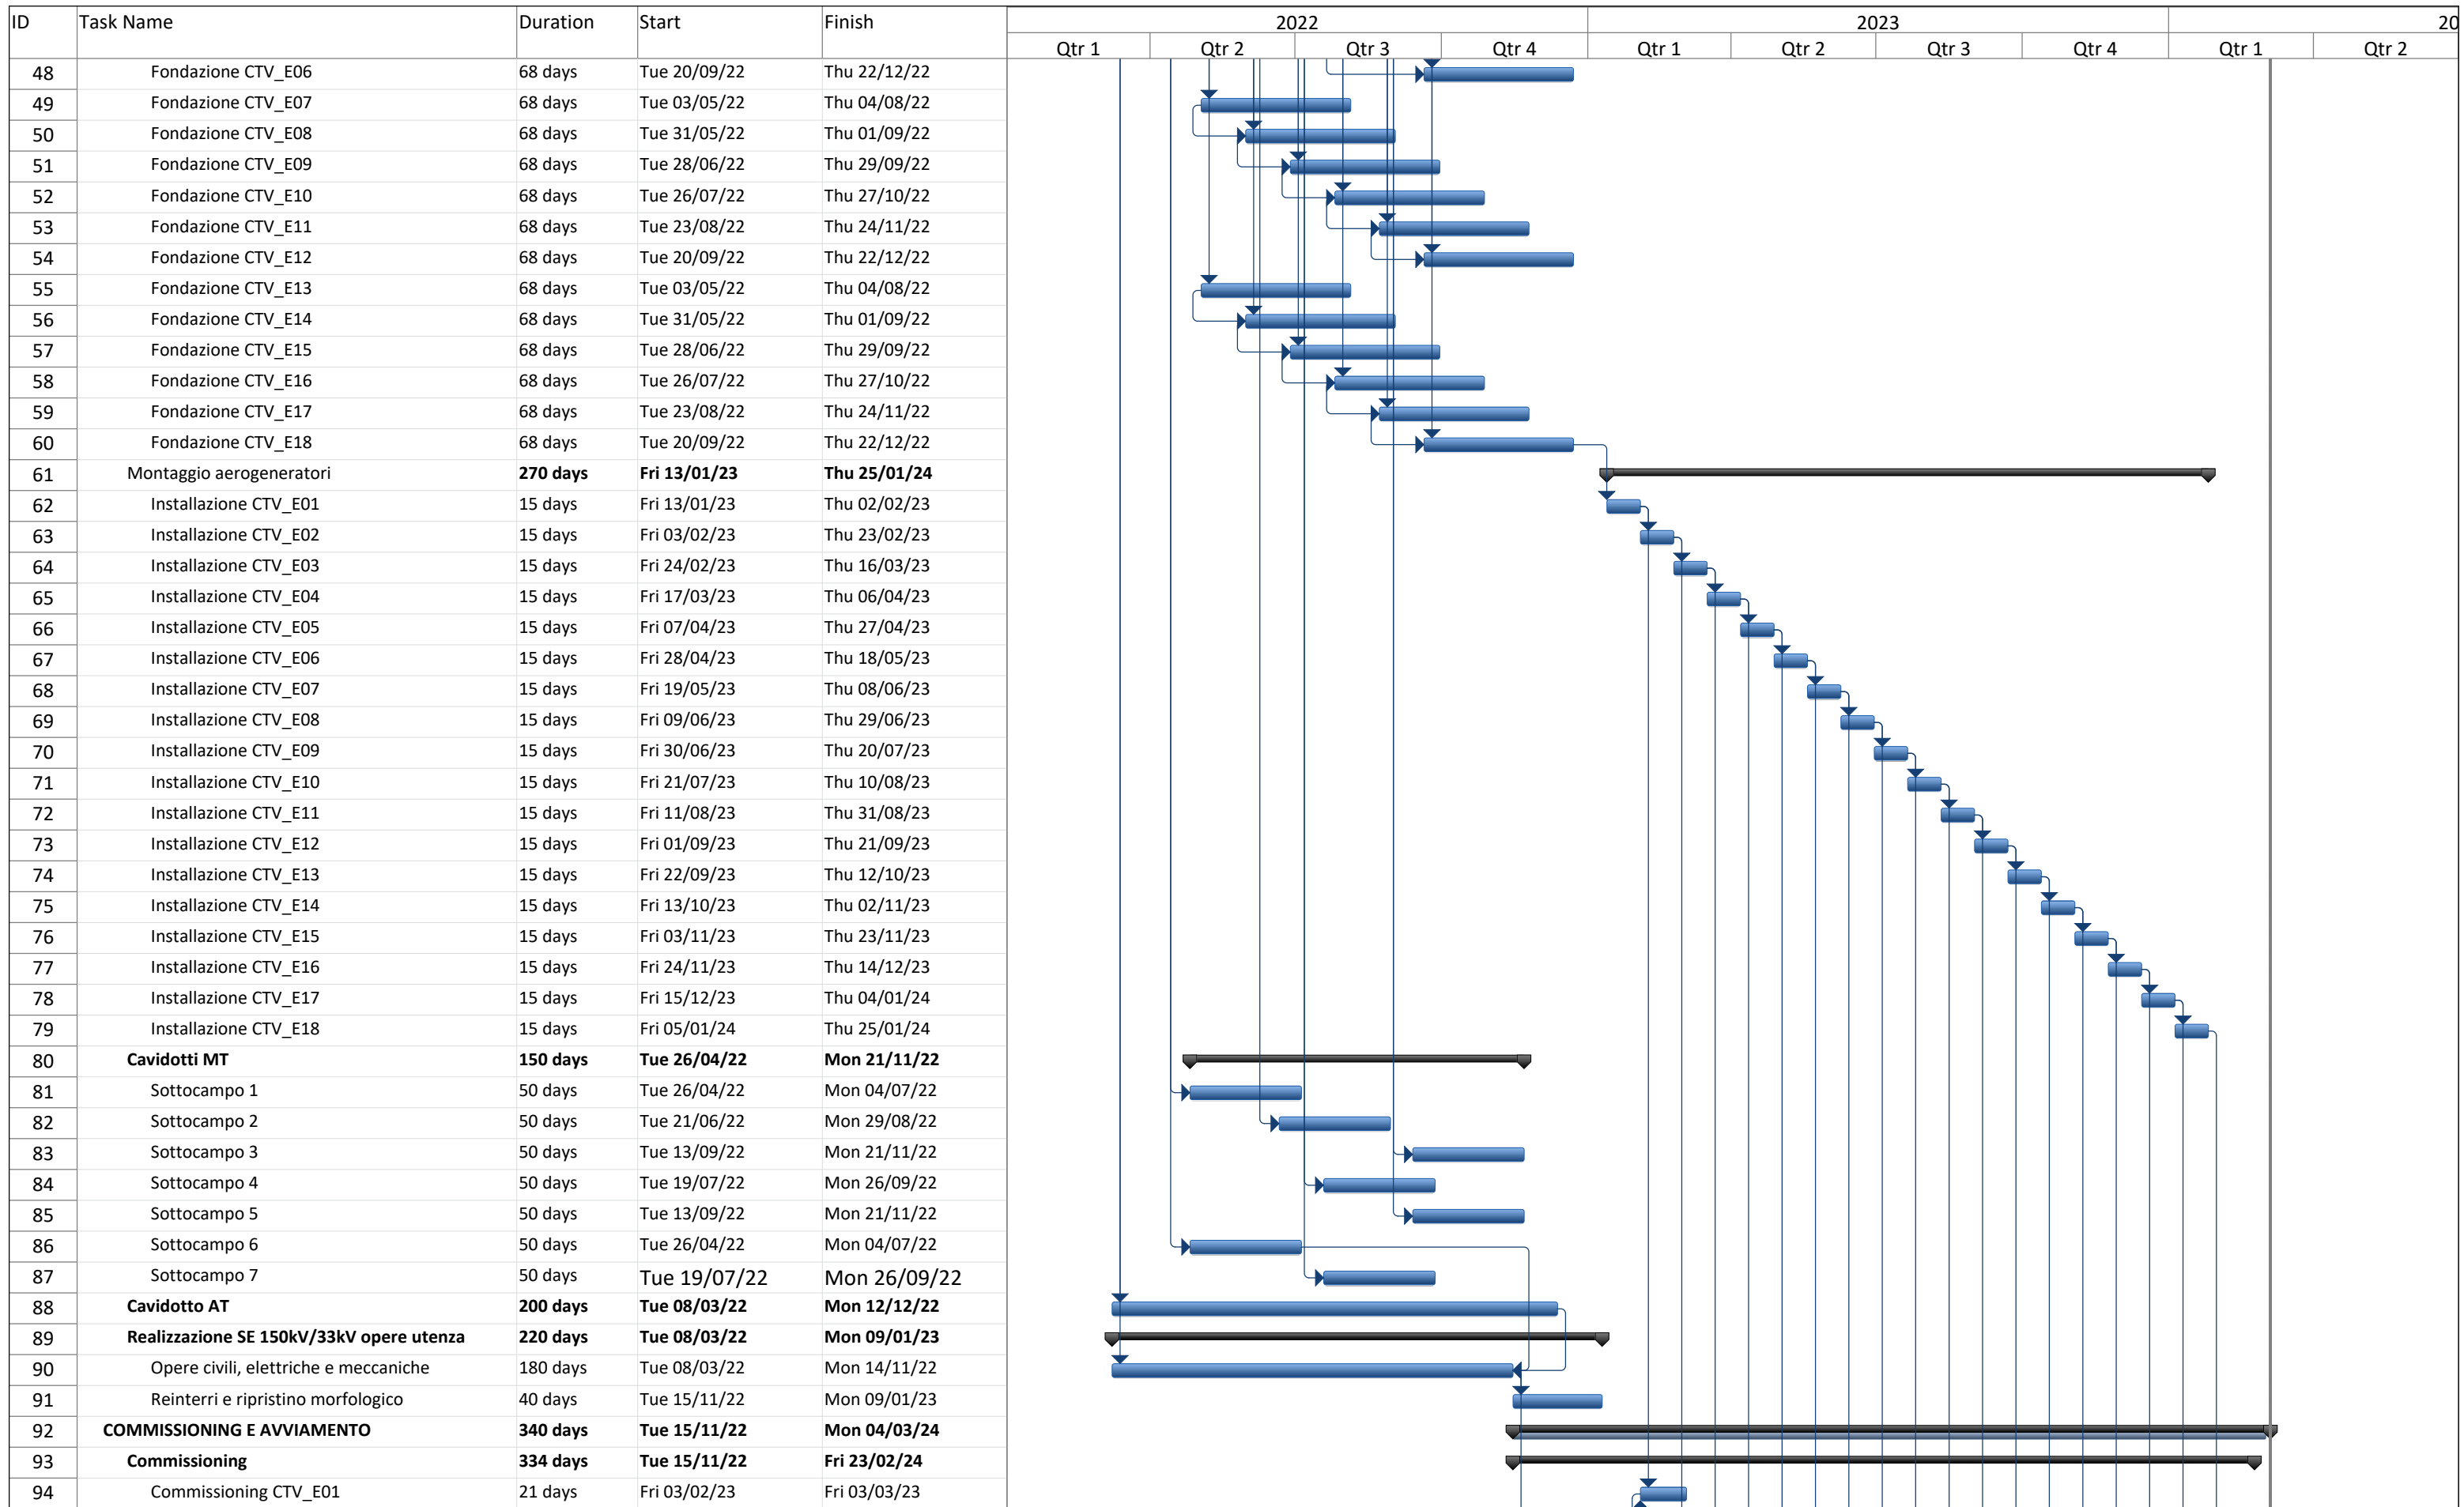

Project: Cronoprogramma
Date: Mon 01/02/21

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Slippage	
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	Start	Finish	2022				2023				20			
					Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2		
95	Commissioning CTV_E02	21 days	Fri 24/02/23	Fri 24/03/23												
96	Commissioning CTV_E03	21 days	Fri 17/03/23	Fri 14/04/23												
97	Commissioning CTV_E04	21 days	Fri 07/04/23	Fri 05/05/23												
98	Commissioning CTV_E05	21 days	Fri 28/04/23	Fri 26/05/23												
99	Commissioning CTV_E06	21 days	Fri 19/05/23	Fri 16/06/23												
100	Commissioning CTV_E07	21 days	Fri 09/06/23	Fri 07/07/23												
101	Commissioning CTV_E08	21 days	Fri 30/06/23	Fri 28/07/23												
102	Commissioning CTV_E09	21 days	Fri 21/07/23	Fri 18/08/23												
103	Commissioning CTV_E10	21 days	Fri 11/08/23	Fri 08/09/23												
104	Commissioning CTV_E11	21 days	Fri 01/09/23	Fri 29/09/23												
105	Commissioning CTV_E12	21 days	Fri 22/09/23	Fri 20/10/23												
106	Commissioning CTV_E13	21 days	Fri 13/10/23	Fri 10/11/23												
107	Commissioning CTV_E14	21 days	Fri 03/11/23	Fri 01/12/23												
108	Commissioning CTV_E15	21 days	Fri 24/11/23	Fri 22/12/23												
109	Commissioning CTV_E16	21 days	Fri 15/12/23	Fri 12/01/24												
110	Commissioning CTV_E17	21 days	Fri 05/01/24	Fri 02/02/24												
111	Commissioning CTV_E18	21 days	Fri 26/01/24	Fri 23/02/24												
112	Commissioning SSE	15 days	Tue 15/11/22	Mon 05/12/22												
113	1° parallelo con rete elettrica	0 days	Fri 23/02/24	Fri 23/02/24												
114	Avviamento	5 days	Mon 26/02/24	Fri 01/03/24												
115	Entrata in esercizio - COD	0 days	Fri 01/03/24	Fri 01/03/24												
116																



Project: Cronoprogramma Date: Mon 01/02/21	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Slippage	
	Summary		Inactive Task		Duration-only		Finish-only			
